Date 08/11/2023 **Certificate Serial No/Ref:**



Landlord Certificate Ltd Electrical Installation Condition Report

10899895

		(Requirements for Electrical Installations – BS 7671 IET 18th Edition Wiring Regulations)
A. DETAIL	S OF THE CLI	IENT OR PERSON ORDERING THE WORK
Name:	Ivan Jossang	
Address:	Flat 9, 58 Cadogar	n Square , London , SW1X 0JW Email: N/A
B. REASO	N FOR PROD	UCING THIS REPORT
Change of o	ccupancy	
		Date(s) inspection and testing carried out: 08/11/2023
C. DETAIL	S OF THE INS	STALLATION WHICH IS THE SUBJECT OF THIS REPORT
Occupier:	Empty	
Address:	Flat 9 58 Cadoga	an Square London SW1X 0JW
Description o	of premises:	✓ Domestic N/A Commercial N/A Industrial N/A Other, please specify :
Estimated ag	e of the wiring sy	ystem Years Years Evidence of additions or alterations N/A Yes N/A No N/A Not apparent
Installation re (Regulation 6	ecords available? 321.1)	Yes N/V No N/A Date of last inspection N/A Sestimated age Alternative source of supply ears (as described in attached schedule if applicable) N/A
D EXTENT	T AND LIMITA	TIONS OF INSPECTION AND TESTING The inspection and testing detailed in this report and accompanying schedules have been carried out in accordance with BS 7671 as amended
Agreed limita	ations including t	ation covered by this report This report covers the inspection and testing of the fixed wiring of the named property with the exception of any agreed limitations as documented and t The reasons, see Regulations 653.2
No access to	the main cut out rus	se to verify type and rating.
Limitations	agreed with	N/A Position (if applicable) N/A
Operational lincluding the		None
		ealed within trunking and conduits, under floors, in roof spaces, and generally within the fabric of the building or underground, have not been inspected the client and inspector prior to the inspection. An inspection should be made within accessible roof space housing other electrical equipment.
E. SUMMA	ARY OF THE C	CONDITION OF THE INSTALLATION
General co	ondition of the	e installation (in terms of electrical safety)
Satisfactory		
		Overall assessment of the installation in terms of its suitability for continued use:
		SATISFACTORY

An unsatisfactory assessment indicates that dangerous (code C1) and/or potentially dangerous (code C2) conditions have been identified

F.R	ECO	MM	END	ATI	ON	5

Where the overall assessment of the suitability of the installation for continued use on page 1 is stated as UNSATISFACTORY, I/we recommend that any observations classified as 'Danger present' (Code C1) or 'Potentially dangerous' (Code C2) are acted upon as a matter of urgency. Investigation without delay is recommended for observations identified as 'Further investigation required' (FI) Observations classified as 'improvement recommended' (Code C3) should be given due consideration.

Subject to the necessary remedial action being taken, I/we recommend that the installation is further inspected and tested by


08/11/2028

G. DECLARATION

I/We, being the person(s) responsible for the inspection and testing of the electrical installation (as indicated by my/our signature(s) below), particulars of which are described above, having exercised reasonable skill and care when carrying out the inspection and testing, hereby declare that the information in this report, including the observations and the attached schedules, provides an accurate assessment of the condition of the electrical installation taking into account the stated extent and limitations in section D of this report.

INSPECTED AND	TESTED BY:		REPORT AUTHOR	ISED FOR ISSUE BY:	
Name (CAPITALS)	RICHMOND BOATEY		Contractor	Landlord Certificate Ltd	
Signature			Address	11 Hatch Lane Chingford, London E4 6LP	
Position	Electrical Engineer	Date 08/11/2023	Name		
Contact	Tel 02037725958		Name	Richmond Boatey	
	Email		Signature		
	Web www.landlord-certificate	es.co.uk	ENROLMENT NO (If applicable)	Napit 61669	Date 08/11/2023

H. SCHEDULES	The attach	ed schedule(s) are part of this document and this r	report is valid	only when they are attached to it
	N/A	Schedule(s) of inspection and	N/A	Schedule(s) of test results attached

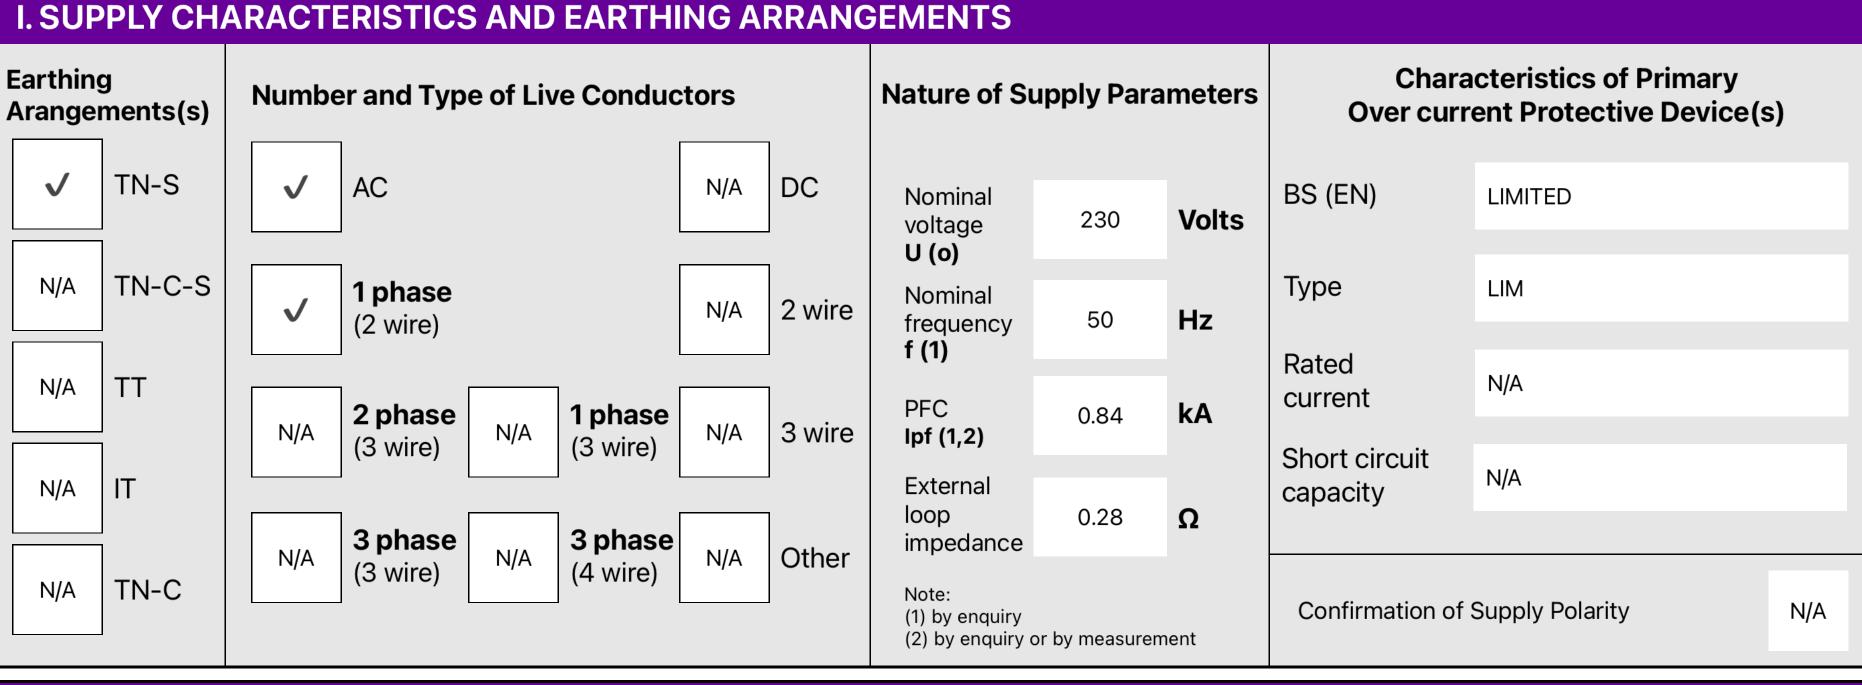

J. PARTIC	ULARS C	OF INS	TALLA	ΓΙΟΝ REFERR	ED T	O IN TH	IS RE	PORT						
Moone of or	orthina	√	Distribu	itor's facility		Туре			N/A		Re	esistance to earth	N/A	Ω
Means of ea		N/A Installation earth electro				Location	e earth ele	ectrode e applicable)						
MAIN PRO	FECTIVE C	CTORS (1	to extraneous c	onduc	ctive parts	s)		MAIN SWITC	H/SWI	TCH-FUSE	CIRCUIT BREAK	ER/RC	D	
Earthing Con	tive nductor		Main B ∃Water	onding		Turo DC (ENI)	600	0.47 tupo P	Voltage rating	230	v			
Conductor Material	Copper		nductor terial	Copper	N/A	N/A installation pipes	N/A	Structural steel	Type BS (EN) No of poles		947 type B 2	Current Rating	100	Α
Conductor Csa mm ²	16		nductor nm ²	10	V	Gas installation pipes	N/A	Other (specify)	Supply		Copper	*Rated time delay	N/A	ms
Connection/ continuity verified			nection/ tinuity verif	ied 🗸	N/A	Oil installation	llation		Conductor		16	*Rated RCD Operating current	N/A	mA
continuity verified V						⊐ pipes			* If RCD main s	witch		*RCD Operating time	N/A	ms

K. OBS	SERVATIONS		
	g to the attached schedules of inspection on and testing section	and test results, and subject to the limitations specified at the Extent and	d Limitations of the
N/A	No remedial action is required	✓ The following observations are made	
ITEM NO		OBSERVATION	CLASSIFICATION CODE
1	No SPD device installed.		C3
N/A	Additional observations	Additional notes/observations attached or to follow ref:	N/A
One of t	he following codes, as appropriate, has been ion the degree of urgency for remedial action	allocated to each of the observations made above to indicate to the person(s) responsible for the
C1 – Dar	nger present. Risk of injury. Immediate remed	dial action required	
	entially dangerous – urgent remedial action provement recommended	required	
	her investigation required without delay		

DISTRII	BUTION BOARD D	ETAILS FOR	Flat 9	58 Cadogar	Square	SW1X 0JW								
DB ref:	DB1	Zs at this board (Ω):		lpf at this board (kA):		Main switch type BSEN		Rating:	A	SPD Type(s)	Supply	mm ²	Earth:	mm ²
Distribution board loc		Phase S Confirm (where app			Supplie from:	d		No. Of phases:	devi	ply protectiv ce type N reference			Rating:	Amps
CIRCU	IRCUIT DETAILS TEST RESULTS													

					Cir	cuit uctors		Overce	urrent	protecti	ve devic	e		RCD				C	ontinuit	y Ω		Insulation resistance							RC	CD .	AFDD					
reference	Circuit designation	f wiring	_	points served	(mm²)	(mm²)	onnection time	(EN)	0	ō	capacity (kA)	100% (Δ) sz pe	(EN	0	(mA)	(A)	circ	ing fin cuits c	only	All cir (At least to be cor	1 column	age V	e (MΩ)	ral (MΩ)	Earth (ΜΩ)	Earth (ΜΩ)	Polarity	easured Zs Ω	time (ms)	button/fucntionality	t button/ ality					
Circuit r	Circuit designation	Type of	Reference	Number of p	Live (m	m) odo	Max discon	Type BS	Туре	Rating	Breaking cap	Max permitted	Type BS	— /^ <i>—</i>	Typ IΔn (r Rating		Tyr IΔn (ι Rating				~ 호 년		r ₁ (line) r _n (neutral) r ₂ (cpc)		(R ₁ + R ₂)	R ₂	Test voltage	Live - Live	Live - Neutral	Live - Eart	Neutral - Ea	Pol	Maximum me	Disconnection	Test button/fu	Manual test button functionality
1	Main Switch							60947	В	100			N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	500	N/A				N/A		N/A	N/A	N/A					
2	Sockets	А	А	10	2.5	1.5	0.4	61009	В	32	6	1.37	61009	В	30	32	0.43	0.41	0.68	0.14	N/A	500v	N/A	500	500	500	✓	0.42	20.6	√	N/A					
3	Sockets	Α	Α	6	2.5	1.5	0.4	61009	В	32	6	1.37	61009	В	30	32	0.35	0.33	0.61	0.12	N/A	500	N/A	500	500	500	√	0.40	22.3	√	N/A					
4	Lights	А	Α	6	1.5	1.0	0.4	61009	В	6	6	7.28	61009	В	30	6	N/A	N/A	N/A	0.20	N/A	500v	N/A	500	500	500	√	0.48	19.6	√	N/A					
5	Lights	Α	Α	8	1.5	1.0	0.4	61009	В	6	6	7.28	61009	В	30	6	N/A	N/A	N/A	0.27	N/A	500	N/A	500	500	500	√	0.55	22.4	✓	N/A					
6	Doorbell	Α	А	1	1.5	1.0	0.4	61009	В	6	6	7.28	61009	В	30	6	N/A	N/A	N/A	0.22	N/A	500	N/A	500	500	500	✓	0.50	19.8	√	N/A					
7	Spare	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A					

Not all SPDs have visible functionality indication. RCD effectiveness is verified using an alternating current test at rated residual operating current (lan). Not all AFDDs have a test button



		TEST INST	RUMENTS USED		
Earth fault loop im	pedance	N/A		RCD	N/A
Insulation re	esistance	N/A		MFT	2253023
C	ontinuity	N/A		Other	N/A
Inspected by: Signature			Name (CAPITALS) Date of inspection	RICHMONI 08/11/2023	

EICR IMAGES	
Engineers optional images of C1 or C2 observations if applicable	
	Item No: 1

	SPECTION SCHEDULE FOR A DISTRIBUTION BOARD INSTALLATION Acceptable Unacceptable Improvement Further Not Verified:	Limitation: Not Applicable:
Outc	omes Acceptable Condition √ Unacceptable condition C1 or C2 Improvement recommended C3 Further investigation: FI Not Verified: NV	LIM N/A OUTCOME
ТЕМ	DESCRIPTION	(Use codes above. Provide additional commen where appropriate. C1, C2, C3 and FI coded items be recorded in Section K of the Condition Report
1.0	INTAKE EQUIPMENT (VISUAL INSPECTION ONLY) An outcome against an item in this section, other than access to live parts, should not be used to determine the overall outcome	
1.1	Condition of service cable	✓
	Condition of service head	✓
	Condition of distributor's earthing arrangement	✓
	Condition of meter tails - Distributor/Consumer	✓
	Condition of metering equipment isolator (where present)	✓
	Condition of isolator (where present)	N/A
2.0	PRESENCE OF ADEQUATE ARRANGEMENTS FOR OTHER SOURCES SUCH AS MICROGENERATORS (551.6; 551.7)	N/A
3.0	EARTHING AND BONDING ARRANGEMENTS (411.3, Chapter 54)	
3.1	Presence and condition of distributor's earthing arrangement (542.1.2.1; 542.1.2.2)	✓
3.2	Presence and condition of earth electrode connection where applicable (542.1.2.3)	N/A
3.3	Provision of earthing/bonding labels at all appropriate locations (514.13)	✓
3.4	Adequacy of earthing conductor size (542.3, 543.1.1)	✓
3.5	Accessibility and condition of earthing conductor at MET (543.3.2)	✓
3.6	Adequacy of main protective bonding conductor sizes (544.1)	✓
3.7	Condition and accessibility of main protective bonding conductor connections (411.3.1.2; 543.3.2; 544.1.2)	√
3.8	Accessibility and condition of other protective bonding connections (543.3.1; 543.3.2)	✓
4.0	CONSUMER UNIT OR DISTRIBUTION BOARD	
4.1	Adequacy of working space / accessibility to consumer unit / distribution board (132.12; 513.1)	✓
4.2	Security of fixing (134.1.1)	✓
4.3	Condition of enclosure(s) in terms of IP rating etc (416.2)	✓
4.4	Condition of enclosure(s) in terms of fire rating etc (421.1.201; 526.5)	✓
4.5	Enclosure not damaged or deteriorated so as to impair safety (651.2)	√
4.6	Presence of main linked switch (as required by 462.1.201)	✓
4.7	Operation of main switch - (functional check) (643.10)	✓
4.8	Manual operation of circuit breakers and RCDs to prove disconnection (643.10)	✓
4.9	Correct identification of circuit details and protective devices (514.8.1; 514.9.1)	✓
4.10	Presence of RCD six-monthly test notice, where required (514.12.2)	✓
4.11	Presence of alternative supply warning notice at or near consumer unit/distribution board (514.15)	✓
	Presence of other required labelling (please specify) (Section 514)	✓
4.13	Compatibility of protective devices, bases and other components; correct type and rating (No signs of unacceptable thermal damage, arcing or overheating) (411.3.2; 411.4; 411.5; 411.6; Sections 432, 433)	✓

N. IN	SPECTION SCHEDUI	LE FOR A DISTRIB	UTION BOARD IN	STALLATION			
Outc	omes Acceptable Condition √	Unacceptable condition C1 or C2	Improvement recommended C3	Further investigation: FI	Not Verified: NV	Limitation: LIM	Not Applicable: N/A
ITEM			DESCRIPTION			(Use codes above. where appropriate. C1	JTCOME Provide additional comment 1, C2, C3 and FI coded items to on K of the Condition Report)
4.14	Single-pole switching of	or protective devices	in line conductor only	y (132.14.1; 530.3.3)			✓
4.15	Protection against mecl 522.8.5; 522.8.11)	hanical damage whe	re cables enter consu	mer unit/distribution boa	rd (522.8.1;		✓
4.16	, ,	tromagnetic effects v	vhere cables enter co	nsumer unit/distribution b	oard/		✓
4.17	RCD(s) provided for fau	ult protection - includ	es RCBOs (411.4.204	l; 411.5.2; 531.2)			N/A
4.18	RCD(s) provided for add	ditional protection/re	quirements - include	s RCBOs (411.3.3; 415.1)			✓
4.19	Confirmation of indicati	ion that SPD is functi	onal (651.4)				С3
4.20	Confirmation that ALL co terminals and are tight a		, including connection	s to busbars, are correctly	located in		✓
4.21	Adequate arrangement (551.6)	ts where a generating	set operates as a sw	ritched alternative to the p	ublic supply		N/A
4.22	Adequate arrangement	ts where a generating	g set operates in para	llel with the public supply	(551.7)		N/A
5.0	FINAL CIRCUITS						
5.1	Identification of conduc	ctors (514.3.1)					√
5.2	Cables correctly suppor	rted throughout thei	r run (521.10.202; 52	2.8.5)			√
5.3	Condition of the insulati	tion of live parts (416	.1)				✓
5.4	Non-sheathed cables printegrity of conduit and	rotected by enclosur I trunking systems (n	re in conduit, ducting netallic and plastic)	or trunking (521.10.1) To i	nclude the		✓
5.5			· · · · · · · · · · · · · · · · · · ·	the type and nature of ins	stallation		√
5.6	Coordination between o	conductors and overl	oad protective device	es (433.1; 533.2.1)			✓
5.7	Adequacy of protective	devices: type and ra	ted current for fault p	protection (411.3)			✓
5.8	Presence and adequacy	y of circuit protective	conductors (411.3.1;	Section 543)			✓
5.9	Wiring system(s) approp	priate for the type and	d nature of the installa	tion and external influence	s (section 522)		✓
5.10	Concealed cables instal	lled in prescribed zoı	nes (see Section D. Ex	tent and limitations) (522	2.6.202)		✓
5.11	-		•	thin earthed wiring system e (see Section D. Extent an	•		✓
5.12	Provision of additional r	requirements for prot	tection by RCD not ex	ceeding 30 mA			
*	For all socket-outlets of	f rating 32 A or less, ı	unless an exception is	s permitted (411.3.3)			✓
*	For the supply of mobile	e equipment not exce	eeding 32 A rating for	use outdoors (411.3.3)			✓
*	For cables concealed in	walls at a depth of le	ess than 50 mm (522	6.202; 522.6.203)			√
*	For cables concealed in	walls/partitions con	taining metal parts re	gardless of depth (522.6.	203)		✓
*	Final circuits supplying	luminaires within do	mestic (household) p	remises (411.3.4)			✓
5.13	Provision of fire barriers	s, sealing arrangeme	nts and protection ag	ainst thermal effects (Se	ction 527)		✓
5.14	Band II cables segregate	ed or separated from	Band I cables (528.1)			√
5.15	Cables segregated or se	eparated from comm	unication cabling (52	28.2)			√
5.16	Cables segregated or se	eparated from non-e	lectrical services (52	8.3)			√

N. IN	SPECTION SCHEDULE FOR A DISTRIBUTION BOARD INSTALLATION								
Outco	mes Acceptable Unacceptable Condition √ Unacceptable condition C1 or C2 Improvement recommended C3 Further investigation: FI Not Verified: NV	Limitation: Not Applicable: N/A							
ITEM	DESCRIPTION	OUTCOME (Use codes above. Provide additional comment where appropriate. C1, C2, C3 and FI coded items to be recorded in Section K of the Condition Report)							
5.17	Termination of cables at enclosures – indicate extent of sampling in Section D of the report (Section 526)								
*	Connections soundly made and under no undue strain (526.6)	✓							
*	No basic insulation of a conductor visible outside enclosure (526.8)	✓							
*	Connections of live conductors adequately enclosed (526.5)	✓							
*	Adequately connected at the point of entry to enclosure (glands, bushes etc) (522.8.5)	✓							
5.18	Condition of accessories including socket-outlets, switches and joint boxes (651.2(v))	✓							
5.19	Suitability of accessories for external influences (512.2)	✓							
5.20	Adequacy of working space/accessibility to equipment (132.12; 513.1)	✓							
5.21	Single-pole switching or protective devices in line conductors only (132.14.1, 530.3.2)	✓							
6.0	LOCATION(S) CONTAINING A BATH OR SHOWER								
6.1	Additional protection for all low voltage (LV) circuits by RCD not exceeding 30 mA (701.411.3.3)	✓							
6.2	Where used as a protective measure, requirements for SELV or PELV met (701.414.4.5)	N/A							
6.3	Shaver supply units comply with BS EN 61558-2-5 formerly BS 3535 (701.512.3)	✓							
6.4	Presence of supplementary bonding conductors, unless not required by BS 7671:2018 (701.415.2)	N/V							
6.5	Low voltage (e.g. 230 V) socket-outlets sited at least 2.5 m from zone 1 (701.512.3)	√							
6.6	Suitability of equipment for external influences for installed location in terms of IP rating (701.512.2)	✓							
6.7	Suitability of equipment for installation in a particular zone (701.512.3)	✓							
6.8	Suitability of current-using equipment for particular position within the location (701.55)	✓							
7.0	OTHER PART 7 SPECIAL INSTALLATIONS OR LOCATIONS								
/ • I	List all other special installations or locations present, if any (*Record separately the results of particular inspections applied)	N/A							
8.0	PROSUMER'S LOW VOLTAGE ELECTRICAL INSTALLATION(S)								
A.I.	Where the installation includes additional requirements and recommendations relating to Chapter 82, additional inspection items should be added to the checklist	N/A							

*Special installations or locations present, if any.	Details of circuits and/or installed equipment vulnerable to damage when testing and/or remarks

PROS	SUN	/IERS	LOW	VO	LTA	GE IN	ISTA	LLAT	ION	1							
Outco	omes	S A	cceptable ondition	e √		Unacc condit	eptable ion C1 c	e or C2		Improv recomr	ement mended C3	Further investigat	ion: FI	Not Verified NV		Limitation: LIM	Not Applicable: N/A
ITEM										DESCR	IPTION				w	(Use codes above. here appropriate. C1 be recorded in Section	Provide additional comment, C2, C3 and FI coded items to on K of the Condition Report)
8.2																	N/A
8.3																	N/A
8.4																	N/A
8.5																	✓
8.6																	N/A
8.7																	N/A
8.8																	N/A
8.9																	N/A
8.10																	N/A
8.11																	N/A
8.12																	N/A
8.13																	N/A
8.14																	N/A
8.15																	N/A
8.16																	N/A
8.17																	N/A
8.18																	N/A
8.19																	N/A
8.20																	N/A
8.21																	N/A
8.22																	N/A
8.23																	N/A
8.24																	N/A
8.25																	N/A
8.26																	N/A
8.27																	N/A
8.28																	N/A
8.29																	N/A
8.30																	N/A
8.31																	N/A
8.32																	N/A
8.33																	N/A

CONDITION REPORT GUIDANCE FOR RECIPIENTS

This report is an important and valuable document which should be retained for future reference

- 1 The purpose of this Report is to confirm, so far as reasonably practicable, whether or not the electrical installation is in a satisfactory condition for continued service (see Section E). The Report should identify any damage, deterioration, defects and/or conditions which may give rise to danger (see Section K).
- 2 This Report is only valid if accompanied by the Inspection Schedule(s) and the Schedule(s) of Circuit Details and Test Results.
- 3 The person ordering the Report should have received the 'original' Report and the inspector should have retained a duplicate.
- 4 The 'original' Report should be retained in a safe place and be made available to any person inspecting or undertaking work on the electrical installation in the future. If the property is vacated, this Report will provide the new owner/occupier with details of the condition of the electrical installation at the time the Report was issued.
- 5 Section D (Extent and Limitations) should identify fully the extent of the installation covered by this Report and any limitations on the inspection and testing. The inspector should have agreed these aspects with the person ordering the Report and with other interested parties (licensing authority, insurance company, mortgage provider and the like) before the inspection was carried out.
- 6 Some operational limitations such as inability to gain access to parts of the installation or an item of equipment may have been encountered during the inspection. The inspector should have noted these in Section D.
- 7 For items classified in Section K as C1 ('Danger present'), the safety of those using the installation is at risk, and it is recommended that a skilled person or persons competent in electrical installation work undertakes the necessary remedial work immediately.
- 8 For items classified in Section K as C2 ('Potentially dangerous'), the safety of those using the installation may be at risk and it is recommended that a skilled person or persons competent in electrical installation work undertakes the necessary remedial work as a matter of urgency.
- 9 Where it has been stated in Section K that an observation requires further investigation (code FI) the inspection has revealed an apparent deficiency which may result in a code C1 or C2, and could not, due to the extent or limitations of the inspection, be fully identified. Such observations should be investigated without delay. A further examination of the installation will be necessary, to determine the nature and extent of the apparent deficiency (see Section F).
- 10 For safety reasons, the electrical installation should be re-inspected at appropriate intervals by a skilled person or persons, competent in such work. The recommended date by which the next inspection is due is stated in Section F of the Report under 'Recommendations'.
- 11 Where the installation includes a residual current device (RCD) it should be tested six-monthly by pressing the button marked 'T' or 'Test'. The device should switch off the supply and should then be switched on to restore the supply. If the device does not switch off the supply when the button is pressed, seek expert advice. For safety reasons it is important that this instruction is followed.
- 12 Where the installation includes an arc fault detection device (AFDD) having a manual test facility it should be tested six-monthly by pressing the test button. Where an AFDD has both a test button and automatic test function, manufacturer's instructions shall be followed with respect to test button operation.
- 13 Where the installation includes a surge protective device (SPD) the status indicator should be checked to confirm it is in operational condition in accordance with manufacturer's information. If the indication shows that the device is not operational, seek expert advice. For safety reasons it is important that this instruction is followed.
- 14 Where the installation includes alternative or additional sources of supply, warning notices should be found at the origin or meter position or, if remote from the origin, at the consumer unit or distribution board and at all points of isolation of all sources of supply.

CODES FOR TYPES OF WIRING												
Α	В	С	D	E	F	G	н	0				
Thermoplastic insulated/ sheathed cables	Thermoplastic cables in metallic conduit	Thermoplastic cables in non-metallic conduit	Thermoplastic cables in metallic trunking	Thermoplastic cables in non-metallic trunking	Thermoplastic SWA cables	Thermoplastic SWA cables	Mineral insulated cables	Other				
